TRAM / PRODUCTION OVERVIEW

01 / 03 Manufacturing performance • Synthetic portfolio data

Reporting month

All

Team

All

Module

All

Completed jobs

5,475

Jobs

Overall labor efficiency

88.8%

Weighted efficiency

Positive overrun hours

4,355.6

Overrun h

Rework rate

13.4%


Rework %

Critical jobs


226

Critical Jobs


Planned vs actual hours by start month

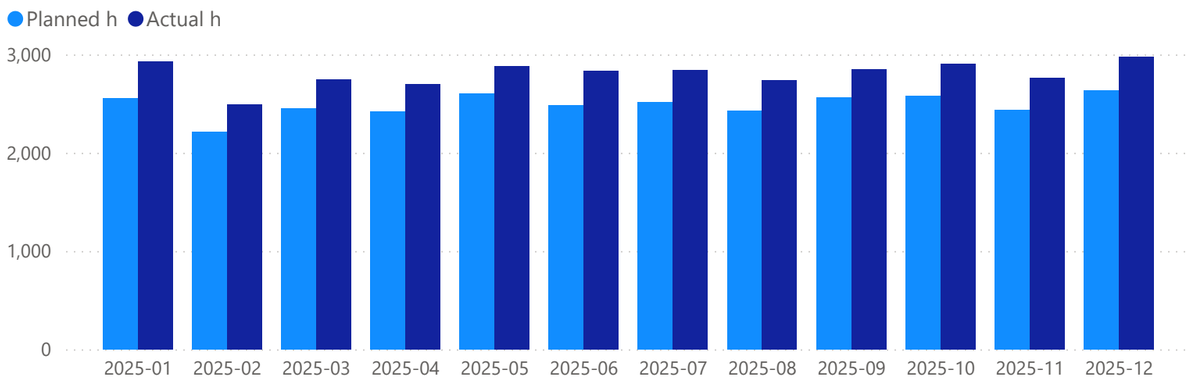

Efficiency: weighted total vs average job

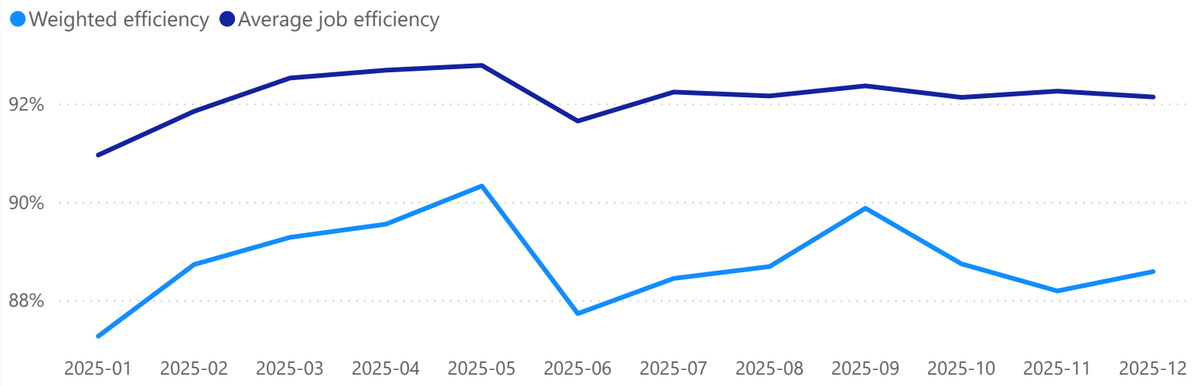

Teams ranked by positive overrun hours

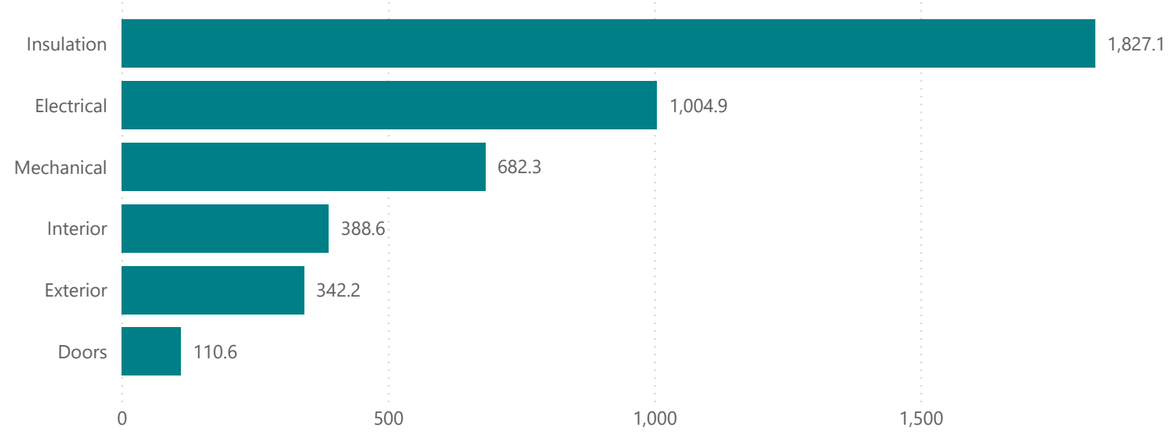

Current selection

5,475 jobs selected | 29,896.2 planned h | 33,676.3 actual h

Selection Summary

Investigation priority

Largest overrun impact: Carbody insulation side wall | 994.9 h

Priority Task

Additional labor measures

Net excess h	Simulated overtime h	Average job efficiency
3,780.1	7,262.7	92.1%

Scope: job start month • All metrics respond to the current selection.

Simulated overtime = hours above 8 per job; not payroll overtime. Rates describe recorded job outcomes.

TRAM / QUALITY & REWORK

02 / 03 Manufacturing performance • Synthetic portfolio data

Reporting month: All

Team: All

Module: All

Jobs in selection: 5,475 Jobs


Pass rate: 63.0% Pass Rate

Rework rate: 13.4% Rework %


Fail rate: 3.5% Fail %

Warning rate: 20.0% Warning rate

Rework and fail rates by start month

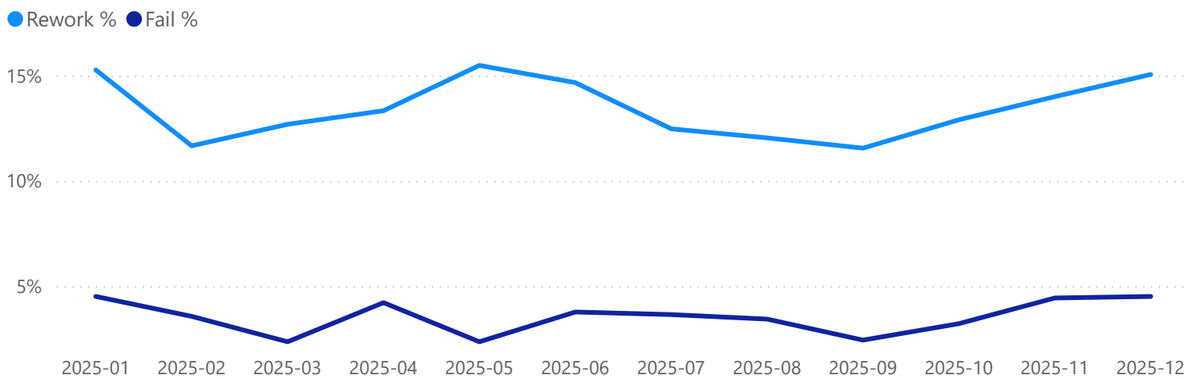

Recorded quality outcomes • job counts

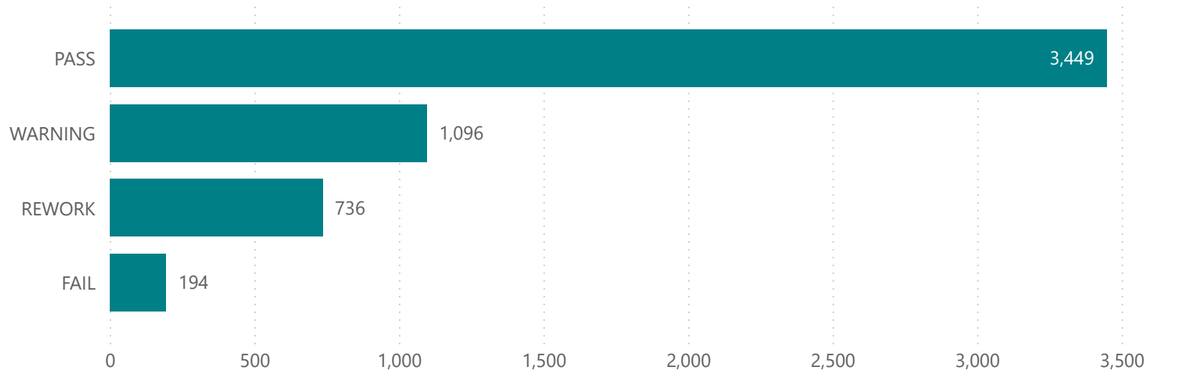

Quality by team • counts beside rates

Team	Jobs	Rework jobs	Rework %	Fail jobs	Fail %
Insulation	936	187	20.0%	55	5.9%
Electrical	970	134	13.8%	36	3.7%
Mechanical	871	124	14.2%	39	4.5%
Exterior	904	121	13.4%	17	1.9%
Interior	922	119	12.9%	32	3.5%
Doors	872	51	5.8%	15	1.7%
Total	**5,475**	**736**	**13.4%**	**194**	**3.5%**

Quality by task • prioritize investigation

Task	Jobs	Rework jobs	Rework %	Fail jobs	Fail %
Roof covers	904	121	13.4%	17	1.9%
Carbody insulation side wall	460	105	22.8%	30	6.5%
Roof insulation	476	82	17.2%	25	5.3%
Interior lighting install	497	78	15.7%	24	4.8%
Interior lighting prep	473	56	11.8%	12	2.5%
Side wall lining	230	43	18.7%	15	6.5%
Rail head lubrication	223	42	18.8%	16	7.2%
Bellows install	224	33	14.7%	7	3.1%
Bumper with absorbers	235	30	12.8%	6	2.6%
Double-leaf doors	429	28	6.5%	5	1.2%
Seats install	226	27	11.9%	5	2.2%
End wall cover	231	26	11.3%	3	1.3%
Driver desk panels	235	23	9.8%	9	3.8%
Sealing strips door set A	443	23	5.2%	10	2.3%
Emergency coupler	189	19	10.1%	10	5.3%
Total	**5,475**	**736**	**13.4%**	**194**	**3.5%**

Scope: job start month • All metrics respond to the current selection.

Simulated overtime = hours above 8 per job; not payroll overtime. Rates describe recorded job outcomes.

TRAM / TASK INVESTIGATION

03 / 03 Manufacturing performance • Synthetic portfolio data

Reporting month All

Team All

Module All

Quality All

KPI status All

Jobs in selection
5,475
Jobs


Positive overrun hours
4,355.6
Overrun h

Net excess hours
3,780.1
Net excess h

Overall labor efficiency
88.8%
Weighted efficiency

Critical jobs
226
Critical Jobs

Tasks ranked by positive overrun hours

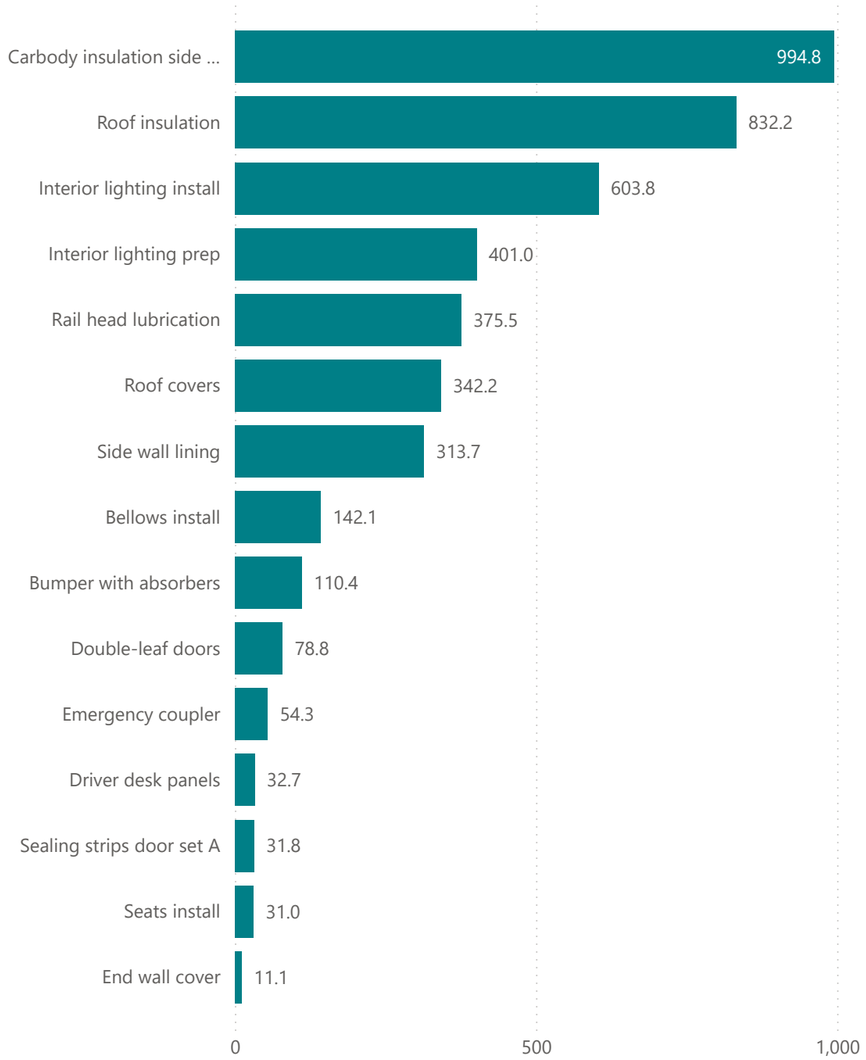

Task evidence • compare volume, hours and quality

Task	Jobs	Planned h	Actual h	Overrun h	Rework jobs	Fail jobs
Carbody insulation side wall	460	4,738.0	5,676.1	994.8	105	30
Roof insulation	476	4,141.2	4,901.1	832.2	82	25
Interior lighting install	497	5,119.1	5,605.9	603.8	78	24
Interior lighting prep	473	3,689.4	4,003.3	401.0	56	12
Rail head lubrication	223	2,453.0	2,796.0	375.5	42	16
Roof covers	904	2,440.8	2,739.3	342.2	121	17
Side wall lining	230	2,760.0	3,010.2	313.7	43	15
Bellows install	224	963.2	1,091.4	142.1	33	7
Bumper with absorbers	235	728.5	826.1	110.4	30	6
Double-leaf doors	429	1,287.0	1,328.0	78.8	28	5
Emergency coupler	189	378.0	427.2	54.3	19	10
Driver desk panels	235	258.5	286.2	32.7	23	9
Sealing strips door set A	443	575.9	588.2	31.8	23	10
Seats install	226	271.2	295.8	31.0	27	5
End wall cover	231	92.4	101.6	11.1	26	3
Total	**5,475**	**29,896.2**	**33,676.3**	**4,355.6**	**736**	**194**

Selected task / team detail

Task ID	Team	Tram unit	Jobs	Actual h	Overrun h
T006	Insulation	UNIT181	5	74.9	23.3
T006	Insulation	UNIT092	6	81.3	19.5
T006	Insulation	UNIT074	6	78.9	18.3
T004	Electrical	UNIT110	6	64.6	17.8
T006	Insulation	UNIT168	7	88.7	17.2
Total			**5,475**	**33,676.3**	**4,355.6**

Scope: job start month • All metrics respond to the current selection.
Simulated overtime = hours above 8 per job; not payroll overtime. Rates describe recorded job outcomes.
